FOR THE COST CONTROL ENGINEER, TO FORWARD TO MANAGEMENT

You cannot optimise steel you have never measured

You asked where AI can help across your operations and named nesting first. We agree, with two changes: we widen *nesting* to *material yield*, and we size the loss from your own Strumis history in four weeks without cutting any steel.

INR 55L	INR 22L	1.46cr	0
FIXED PRICE 16 WEEKS	YOU CAN STOP AT WEEK 4	CONSERVATIVE VALUE A YEAR	TONNES CUT TO MEASURE IT

CONTENTS What this document covers

EIGHT SECTIONS YOU ASKED FOR, AND WHERE EACH ONE SITS

Problem understanding	1 to 2	What you asked against what you need	Evaluation	5	Baseline, threshold, two gates
What you do not know yet	3	Eight ranked questions	Build plan and timeline	5	Sixteen weeks, five dependencies
Solution	3 to 4	Ranked map, five options, six refusals	Cost and value	6	Effort, price, three scenarios
Solution engineering	4	Inputs, solver, sign-off	Risks	6	Eleven, with a leading indicator each

SUMMARY Four weeks from now you know what nesting costs you

THE PROPOSAL IN FOUR BLOCKS

01 · WIDEN THE ASK

Nesting becomes material yield

Waste comes from three places: the cutting layout, the length and size of the stock you buy, and the leftover pieces you reuse. A nesting optimiser addresses one of the three. Our first build addresses all three.

02 · MEASURE FIRST

Replay past nests, cut nothing

We re-plan your closed projects three ways: your hand nest, the Strumis automatic you already own, and our proposal. No steel is cut and nobody changes routine, so it runs while your live projects are on hold.

03 · TWO QUICK WINS

Fleet report week 2, revision register week 3

The first uses CarTrack and the booking system you installed six months ago. The second builds the missing record of revisions so client-caused losses can be claimed back. Both use data you already hold.

04 · STOP GATE

Below the threshold, we stop

If the Advisor does not beat your hand nests by 0.5 percentage points against a measured baseline, you pay INR 22 lakh and we keep the revision register and the fleet report. The negative result is still a result.

DECISIONS I MADE WHERE THE NOTES WERE UNCLEAR

80,000 t a year is steel purchased and processed. Your monthly figure of 7,000 to 8,000 t implies 84,000 to 96,000 t. I plan on 80,000 t, which is 6,667 t a month. Flagged, not silently averaged.

Plate is 15% of tonnage until your 12-month export says otherwise.

Steel at INR 60,000 a tonne, scrap at INR 30,000, so each wasted tonne costs INR 30,000 net, as placeholders for your purchase ledger rates.

AND ONE DISTINCTION I REFUSED TO BLUR

Cost loading is two questions. Reusing an offcut on a later project already happens: “When they nest new projects, they check the offcuts first”.

What is unresolved is whether one *purchased plate* can be shared between two projects, and you said you would “have to check with my team”. **I build against neither.**

01.1 What you asked for, and what you need

THREE OF THE FIVE ROWS ARE NOT WHAT YOU ASKED FOR

YOU ASKED	WHAT YOU NEED
“Where to start, where else, how to improve the process”	A ranked map of every area where AI pays You have no view of which area is worth money, and your contact has to update his office this week.
“AI to optimise nesting” →	Visibility of waste first, then a tool that reduces it You cannot tell how much steel is wasted, how much was avoidable, or what sits unused.
“AI to allocate steel across projects”	A cost-loading ruling from your team first, then software Cost loads to the project that bought it. Software cannot overrule your accounting policy; a decision can.
“Fewer hired-in trailers”	A weekly view from CarTrack and the booking system Both systems record data nobody uses yet. Management is unhappy about the hire-in bill.

NOT ASKED FOR, AND THE CHEAPEST THING IN THE PLAN

A record of drawing revisions and their cause. Revisions arrive with no record, own-error tonnage is unknown, and client-caused losses are claimable. **Each unrecorded revision is a claim you cannot file.** It costs one dropdown on a remake order, which is why it is in phase one rather than phase three.

01.2 The six areas you raised, and where each one lands

FOUR ARE BUILDABLE ON DATA YOU ALREADY HOLD

FIGURE 1 · VERDICT ON EVERY AREA, AND THE VALUE POOL BEHIND IT

NESTING OPTIMISATION
your first pick, our first project

DRAWING REVISIONS
not asked for, cheapest to fix

PLATE SHARING
largest pool, gated on you

TRAILER UTILISATION

BUYING SIZES

WAREHOUSE STORAGE

MATERIAL YIELD 1.2 to 2.4 crore

FLEET 26 L

REVISIONS 48 L


Also on your list, raised once by a colleague who was not on the second call: yard, trailer loading, factory ops. **We ask about all three.**

Cross-project plate sharing is the largest pool in the business and the one thing we will not build: the blocker is an accounting decision, not software.

01.3 Your numbers already agree with each other

PLATE 20 TO 25%, PROFILES 5 TO 10%, OVERALL 7 TO 10%

FIGURE 2 · THE REACHABLE WASTAGE BAND, DERIVED FROM YOUR OWN NUMBERS

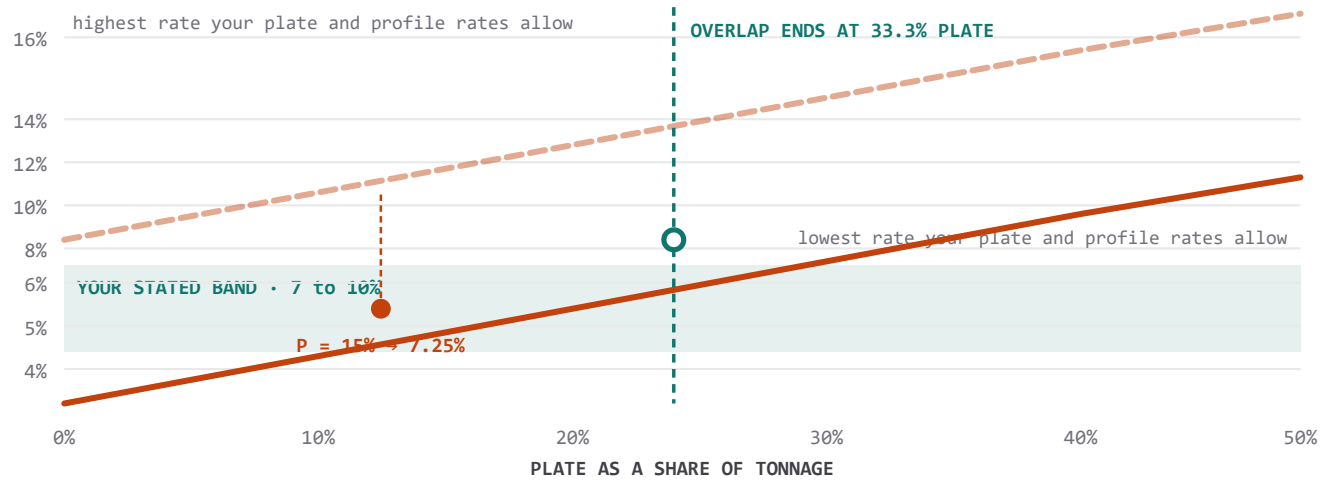

Your three figures are consistent for every plate share up to 33.3%, so no correction is needed. What is missing is the basis behind them, so no baseline can be derived. A P = 15% split at plate 20% and profiles 5% gives 0.15(20) + 0.85(5) = 7.25%, inside your band. I name 15% as a decision your tonnage export replaces in week 1, not as a derivation. At band edges the crossover is bounded between P = 16.7% and 33.3%, so plate share cannot be inferred.


AN ERROR WORTH TELLING YOU ABOUT

An early version of this analysis tested whether the band's *upper* bound fell below 10%, found no solution, and nearly told you your own numbers were wrong. The correct test is whether the bands *overlap*. Right question, wrong edge, and it would have been the first thing you heard from us.

01.4 Six breaks sit along one path

BUSINESS DEVELOPMENT TO DISPATCH

FIGURE 3 · THE AS-IS PROCESS BY LANE, WITH THE SIX LOSS POINTS

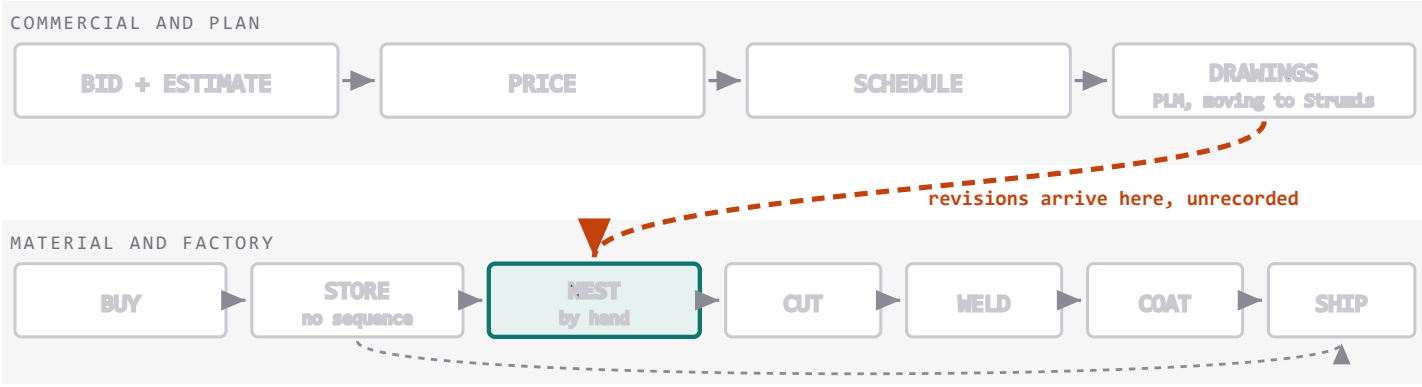

remnants come back to the store, checked by hand against new work

WHERE THE MONEY LEAVES

1. Revisions after release, no record
2. Own-error tonnes uncounted
3. Offcut reuse depends on memory
4. Full sizes bought per project
5. Store yard has no sequence
6. Fleet data stops at reports

Red is where your money leaves. The nesting team says automatic nesting wastes more and nobody has tested it. Offcut reuse already works, but only because a person remembers, and you have said it could be done better. Break 3 is the cheapest to fix and among the largest, because the rule exists and only the instrument does not. You run 13 own trailers and still hire in.

01.5 Who has to say yes, and what each needs to hear

FOUR OF THESE GROUPS HAVE NEVER HAD A CONVERSATION WITH US

WHO	WANTS	WORRIES ABOUT	WHAT WE NEED FROM THEM
Cost Control engineer OUR CONTACT	A forwardable plan and defensible numbers	Sponsoring something he cannot judge. He sees nesting "from the outside"	Sponsor role, the cost-loading answer, report access
Management HIS OFFICE	Fewer hired trailers, lower steel cost	Spending without a result	A decision at week 4 and week 16
Nesting team NEVER ON A CALL	To keep the method they believe saves steel	Software overriding their craft; being blamed for waste	A named approver, two nesters a few hours a week, their rules
Engineering DRAWINGS	Fewer revision problems	Being blamed for own-error losses	Revision history, confirmation of cause labels
Purchasing	Material on site by the project date	Buying early because the schedule demands it	Purchase lines, standard-size rules
Store yard	Faster retrieval of buried material	Extra recording work	Location notes from week 3
Transport and dispatch	Trailers and cranes when needed	Booking rules that change	Booking data, a fairness check on the hire-in list
Planning and estimation	Reliable dates and prices	Dates set before revisions settle	Later: measured loss by product, fed into bids
IT / Strumis owner	A stable migration from PLM	Another integration to maintain	A read-only export route

02 What I need to ask on the next call

RANKED BY HOW MUCH THE ANSWER CHANGES THE PLAN

#	QUESTION	WHY IT MATTERS	ASSUMED UNTIL ANSWERED
1	Can we export read-only from Strumis: nests, parts, stock used, remnants made, purchase lines, revision history?	Decides whether the replay runs in week 3	Nests, stock and purchases export. Revisions are partial
2	Which rules do nesters follow that automatic nesting ignores: direction, bevels, common cuts, cut order, minimum usable offcut?	Explains why they say hand beats auto, and defines the validator	They shape remnants for reuse and respect machine limits that default settings ignore
3	What was tonnage by product and thickness over 12 months, and does 80,000 t mean purchased steel?	Sets plate share and which material carries the loss	Purchased steel, plate 15% of tonnage
4	Can one purchased plate be shared between two projects at book value, and who owns that decision?	Decides whether the largest pool is a build item or only a report	Unresolved. We report missed reuse in rupees and build nothing that depends on the answer
5	How many trailer-days do you hire per month, at what rate, and who approves a hire?	Sizes the fleet saving	90 trailer-days a month at INR 6,000, 40% avoidable
6	How many revisions does a drawing receive, when do they land against nesting, and who tags the cause?	Sizes the claim-back pool and the register design	One to three per drawing, mostly after nesting
7	Who approves a nest, who holds the budget, who signs off the pilot?	The wrong sponsor ends the work	Nesting lead approves, Cost Control manager holds budget
8	What was in the Word document, and what did the other supplier propose and price?	You listed priorities we have not seen	The same six areas


QUESTION 4, BECAUSE THE NOTES ARE EASY TO MISREAD

Two different things get conflated. **Reusing an offcut on a later project already happens. Sharing one purchased plate between two projects is unresolved.** Treating the first as blocked would have deleted the largest value pool from this case and mis-stated your own rule back to you. Treating the second as settled would have built against an accounting policy nobody in this engagement owns.

03.1 Where AI fits, ranked across every area you raised

VALUE POOL AGAINST THE DATA YOU ALREADY HOLD

FIGURE 4 · VALUE AGAINST DATA READINESS

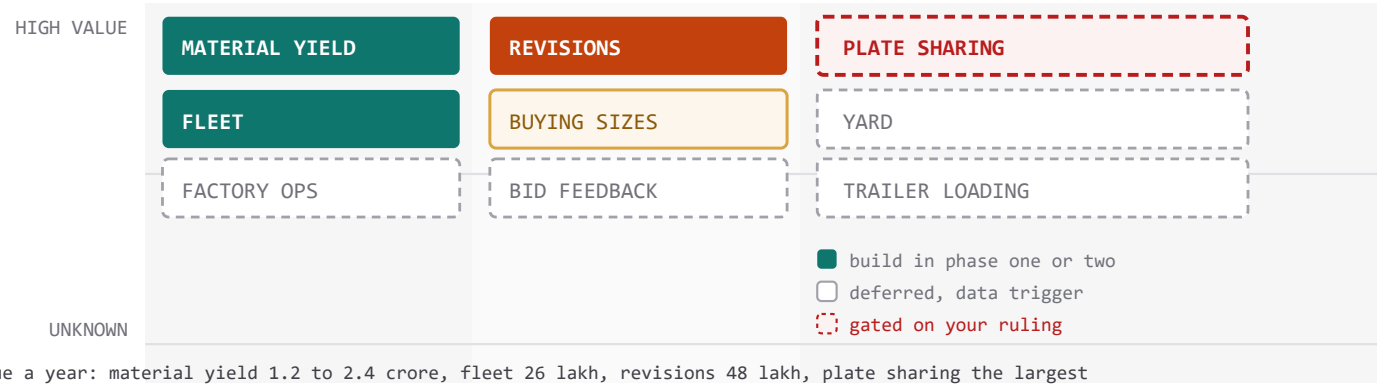

Material yield is the only area with both a large pool and data you already hold. Fleet is a real complaint with a small pool, so it becomes the week-2 quick win rather than the engagement. Plate sharing sits furthest right because it is blocked by your accounting decision, not by software.

03.2 Five options, and why this one

INCLUDING THE OPTION THAT IS ONLY A REPORT

	OPTION	VERDICT	REASON
A	Build a new AI nesting engine	REJECTED	Strumis already has the geometry engine. A new one costs the most and has no baseline to improve on
B	Buy or tune packages	REJECTED	The other supplier offers this. You asked for development and delivery, and nobody would own the integration
C	Measure only and report	REJECTED	Management gets a document with no decision attached, which is billing for an answer you already suspected
D	**Replay benchmark, then a remnant-aware Yield Advisor on top of Strumis, human approved**	PICKED	Largest pool, data exists, answer by week 4, works inside the per-project cost rule, and builds the remnant register that later phases need
E	Start with the fleet	QUICK WIN	Real pain, but about INR 26 lakh a year beside nesting

WHY D FITS YOU SPECIFICALLY

The loss data sits in Strumis already.

A replay needs no steel cut and no shop-floor time, so the result lands in four weeks even with projects on hold. The advisor uses remnants first, so it works inside your cost rule. The remnant register it builds becomes the input to yard storage and to the cross-project question.

WHAT WE WILL DELIBERATELY NOT BUILD

A new 2D geometry engine · cross-project plate sharing · a yard or warehouse system · a trailer load planner · auto-release of nests without a named approver · gain-share in this engagement, offered for phase 3 with a cap


WHY NOT A LIVE A/B TRIAL

Cutting both arms on live projects doubles steel consumption on every nest in the sample and needs live projects you may not have. The replay avoids both problems and still produces paired, comparable arms.

04 Yield Advisor, end to end

READ-ONLY INPUTS, FOUR STAGES, ONE HUMAN SIGN-OFF

FIGURE 5 · WHERE THE DATA COMES FROM AND WHERE A PERSON SIGNS

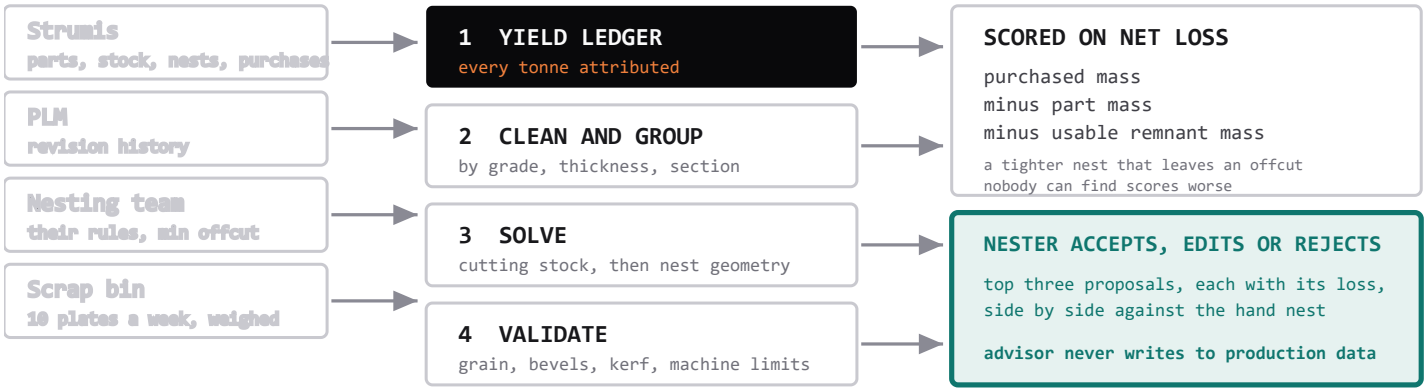

A remnant counts as recovered only above the minimum usable size AND with a recorded location.

Each override carries a reason from a short list, and those reasons update the rules. Everything runs from exports, so your Strumis migration cannot break it, and reports go to the people who already read them.

Four read-only inputs, one ledger that attributes every tonne, four stages, and a person who signs. The Advisor proposes three nests side by side with the hand nest and never writes to production data. Every override reason updates the rules.

REVISION REGISTER, WEEK 3

The model reads revision notices and PLM history, extracts what changed, and proposes a cause plus the parts already cut. **An engineer confirms every label.** Cost Control receives a claim-back list for client-caused losses and a monthly own-error tonnage figure.

FLEET REPORT, WEEK 2, NO MODEL

Idle hours per asset from CarTrack, bookings from the booking system, and each hire-in checked against idle capacity on the day. Dispatch confirms the avoidable list. It lands in the report Cost Control already makes, so it adds no meeting.

FITTING YOUR ROUTINE

The Advisor sits at the step your team already has, between drawing release and the factory. Two short training sessions. The pilot starts in shadow mode, so nobody changes routine until the team trusts the output.

05 How we will know it worked, and when we stop

BASELINE, THRESHOLD IN YOUR MONEY, TWO GATES

FIGURE 6 · THE TWO GATES, AND WHAT HAPPENS AT EACH

GATE 1 · WEEK 4 · REPLAY ON 40 NESTS, NO STEEL CUT

Three arms, same parts
your hand nest
Strumis auto, default and tuned
the Yield Advisor

▶ **GO**
at least 0.5 points
90% bound above zero
80% rated buildable

▶ **TUNE**
0.25 to 0.5 points
two weeks of tuning
then one retest

▶ **STOP**
below 0.25 points
you pay 22 lakh
we stop building

GATE 2 · WEEK 16 · PILOT ON TWO LIVE PROJECTS

Measured, not asserted
against the baseline
and matched hand nests
blind review of 15 pairs

ROLL OUT
at least 0.3 points realised
nester acceptance above 50%

STOP
below 0.3 points after six assisted weeks, or acceptance below 50%

Bootstrap 90% interval on the paired difference per nest. Measured by our data engineer, checked by the nesting approver, co-signed by Cost Control, who weighs scrap from 10 plates a week.

Two gates. At week 4 nothing is cut: forty past nests are replayed and the Advisor has to beat your hand nest by half a point with the lower bound above zero. At week 16 it runs beside you on two live projects, and six assisted weeks below a third of a point ends the build.

WHY HALF A PERCENTAGE POINT, IN YOUR MONEY

One tenth of a percentage point of overall loss is 80 t, which at INR 30,000 net a tonne is **INR 24 lakh a year**. Half a point is 400 t and **INR 1.2 crore a year, more than twice our fixed price**. The gate is set where the prize clears the cost by a wide margin, so the test is worth running even if it is close.

SECONDARY MEASURES, TRACKED FROM WEEK 1

Remnant reuse rate, and time per nest

Revision label agreement against a 90% target on 100 labelled revisions

Idle trailer hours and hired trailer-days a month

WHO MEASURES WHAT

Our data engineer computes from Strumis records


The nesting approver checks it and runs the blind review of 15 pairs

Cost Control co-signs the method and weighs 10 plates a week as an independent check

06 Sixteen weeks, five dependencies, three of them yours in week one

THE FIRST RESULT LANDS IN WEEK 2 AND NEEDS NOTHING BUILT

FIGURE 7 · SIXTEEN WEEKS, AND WHAT WE ARE WAITING ON

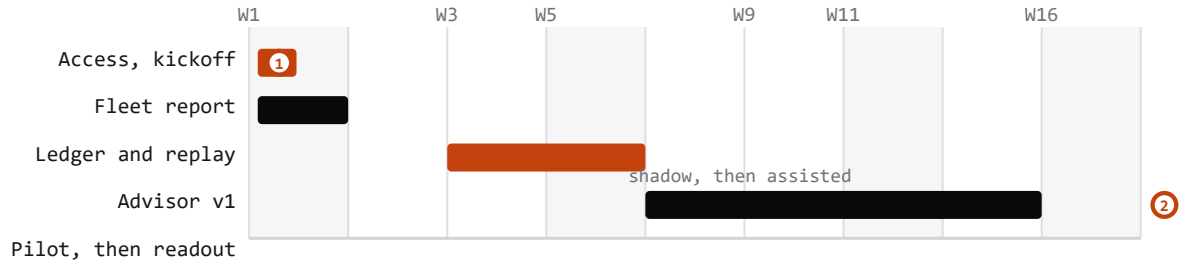

YOU: D1 read-only exports, W1 · D2 named nest approver + two nesters 4 hrs/wk, W1
D3 cost-loading answer, W2 · D4 12-month tonnage export, W1 · D5 two live projects, W8

1 = gate 1, week 4. 2 = gate 2, week 16. The fleet report needs no Strumis access, so a late D1 delays gate 1 by the same number of weeks.

Sixteen weeks, and what each phase is waiting on. The week-2 fleet report needs nothing built, so it lands even if every access request slips. A late Strumis export delays gate 1 by the same number of weeks.

07 What it costs us, what it costs you

128 PERSON-DAYS, INR 33.08 LAKH COST, INR 55 LAKH PRICE

Effort and team

PHASE	DAYS	INR
0 · weeks 1 to 2	20	4.20 lakh
1 · weeks 3 to 8	60	12.96 lakh
2 · weeks 9 to 16	48	10.56 lakh
Labour, 128 days		**27.72 lakh**
Hosting, 16 weeks		1.20 lakh
Contingency, 15%		4.16 lakh
Total cost to us		**33.08 lakh**

Daily costs assumed: FDE lead INR 30,000, ML and optimisation engineer 24,000, data engineer 18,000, analyst 12,000.

Price and payment

MILESTONE	SHARE	INR
Kickoff, week 1	20%	11.0 lakh
Gate 1 replay report, week 4	20%	11.0 lakh
Advisor v1 in staging, week 8	30%	16.5 lakh
Pilot readout, week 16	30%	16.5 lakh
Fixed price, gross margin		**55 lakh, 39.9%**


YOUR DOWNSIDE IS CAPPED

If gate 1 says stop you owe INR 22 lakh and nothing more. That is 40% of the price. Billing front-loads because weeks 1 to 8 carry the delivery risk.

07.1 What you get back, in your money

THREE SCENARIOS. THE CONSERVATIVE CASE IS THE FLOOR, NOT THE PITCH

FIGURE 8 · VALUE A YEAR AGAINST OUR FIXED PRICE

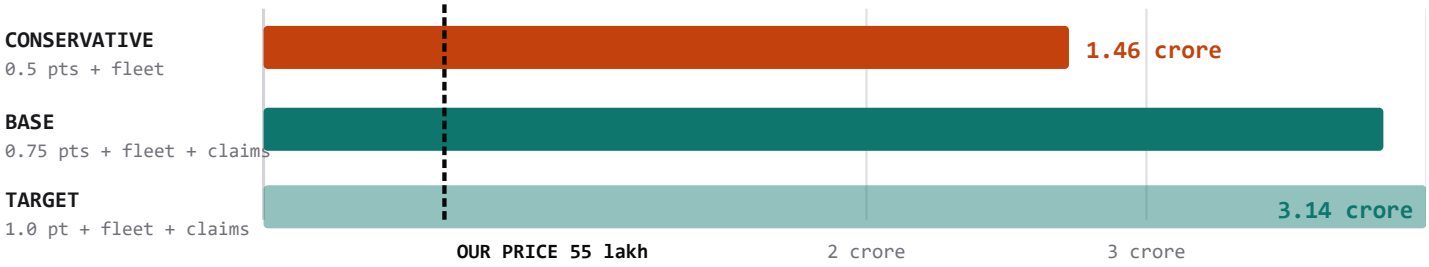

Payback on the conservative case is 55 / (146/12) = 4.5 months of full operation; the base case repays in under three. Savings land one purchase cycle after roll-out, because steel is bought before the nest exists, so plan on a ramp and agree in week one who books the saving.

HOW THE LINES ARE BUILT

Nesting 0.5 pts × 80,000 = 400 t × 30,000 = 1.2 cr

Nesting 0.75 pts = 600 t = 1.8 cr

Fleet 90 × 12 × 6,000 = 64.8 lakh, 40% = 26 lakh

Claim-back 320 t × 60,000 × 25% = 48 lakh

RUNNING COST AFTER WEEK 16

Support retainer 1.5 lakh a month

Hosting 0.4 lakh a month

Model usage, 500 revisions at INR 5 = 0.03 lakh

Third-party fees passed through at cost

SENSITIVITY

Break-even 183 t a year, about 3.5 t a week.

If net loss is INR 20,000/t: 0.80 cr.

If INR 40,000/t: 1.60 cr.

Claim-back is the least certain line, assuming revision scrap of 0.4% of tonnage with 25% recoverable.

08 What could go wrong, and what we do about it

ELEVEN RISKS. TWO ARE HIGH CHANCE AND HIGH IMPACT, AND BOTH SIT WITH YOUR NESTING TEAM

#	RISK	CHANCE	IMPACT	WHAT WE DO
1	Nesting team resists the Advisor	HIGH	HIGH	They approve every nest and own the rules. Blind review of 15 pairs. Their override reasons improve the tool
2	Strumis export is thinner than assumed	MED	HIGH	Question 1 in week 1. Fall back to nest reports and manual extracts for the replay set
3	Replay misses conditions the nesters faced	MED	MED	Rebuild stock by date from the register. Compare only plate-internal yield where we cannot
4	Projects on hold leave too few live nests	MED	MED	Replay carries the proof. Pilot runs on whichever two projects are live
5	Cost-loading rule never changes	HIGH	MED	Value case excludes cross-project plate sharing. We report missed reuse as evidence, in rupees
6	Savings arrive late because steel is bought before nesting	HIGH	MED	Track gain at purchase, not at nesting. Agree who books the saving in week 1
7	Ledger overstates recovery because remnants cannot be found	MED	MED	Location note required before a remnant counts. Weekly scrap weighing as an independent check
8	Strumis migration lands mid-pilot	MED	MED	Work from exports, not the database
9	Language model mislabels revision causes	MED	MED	Engineer confirms every label. Track agreement against the 90% target on 100 labelled revisions
10	My rupee assumptions are wrong	HIGH	MED	Week 1 replaces them with your ledger. The range is shown in the sensitivity line
11	Sponsor or budget changes	LOW	HIGH	Management sees results at weeks 2, 4 and 16, and the stop gate limits exposure

A Assumptions register

TWELVE ASSUMPTIONS, EACH WITH THE QUESTION AND THE WEEK THAT REPLACES IT

ID	ASSUMPTION	REPLACED BY	WHEN
A1	80,000 t is steel purchased and processed a year	Purchase ledger	Week 1
A2	Plate is 15% of tonnage	12-month tonnage export	Week 1
A3	Plate loses 22.5%, profiles 7.5%, the midpoints of your stated ranges	Measured baseline	Week 4
A4	Steel INR 60,000/t, scrap INR 30,000/t, net INR 30,000/t	Purchase ledger, scrap sales	Week 1
A5	90 hired trailer-days a month at INR 6,000, 40% avoidable	Week-2 fleet report	Week 2
A6	Revision-related scrap is 0.4% of tonnage, 25% recoverable	Revision register	Week 8
A7	Minimum usable remnant 500 × 500 mm plate, 1,000 mm profile	Nesting team	Week 1
A8	Cost Control owns the cost-loading rule	Question 4	Week 2
A9	Daily costs INR 30,000 / 24,000 / 18,000 / 12,000 by role	Our finance team	Internal
A10	Hosting INR 0.4 lakh/month, model usage about INR 5 per revision	Quotes at build	Week 5
A11	Strumis exports nests, stock and purchases read-only	Question 1	Week 1
A12	At least two projects are live during weeks 9 to 14	Planning team	Week 8

B The arithmetic, in full

EVERY FIGURE IN THIS CASE STUDY, DERIVED FROM THE REGISTER ABOVE

Band. 0.20P + 0.05(1-P) to 0.25P + 0.10(1-P) = 5%+15P to 10%+15P. Overlaps your 7 to 10% while P ≤ 33.3%.

At P = 15%. 12,000 t × 22.5% = 2,700 t; 68,000 t × 7.5% = 5,100 t. Total 7,800 t = 9.75% of 80,000 t. Across your full ranges, 5,800 to 9,800 t, or 7.25% to 12.25%.

Crossover. At midpoints 22.5P = 7.5(1-P), so P = 25%. At band edges, plate loss 20,000P meets profile loss 4,000(1-P) at P = 16.7%, and plate loss 16,000P meets profile loss 8,000(1-P) at P = 33.3%. Bounded, not a point.

Monthly. 80,000 / 12 = 6,667 t against your 7,000 to 8,000.

Cost. 27,72,000 labour + 1,20,000 hosting + 4,15,800 contingency = 33,07,800.

Margin. (55,00,000 − 33,07,800) / 55,00,000 = 39.9%.

Nesting value. 0.005 × 80,000 = 400 t × 30,000 = 1,20,00,000. 0.0075 × 80,000 = 600 t = 1,80,00,000. 0.010 × 80,000 = 800 t = 2,40,00,000.

Fleet. 90 × 12 × 6,000 × 0.40 = 25,92,000. **Claim-back.** 0.004 × 80,000 = 320 t × 60,000 × 0.25 = 48,00,000.

Payback. 55 / (146/12) = 4.5 months. **Break-even.** 55,00,000 / 30,000 = 183 t a year, about 3.5 t a week.

C Deferred areas and their triggers

NOTHING IS DROPPED, ONLY SEQUENCED BEHIND A MEASURABLE TRIGGER

AREA	TRIGGER TO START	DATA NEEDED FIRST
Yard and warehouse storage	Remnant register has two months of location records	Location of each plate and remnant, retrieval time per request
Trailer loading plan	Fleet report shows load factor, not trailer count, is the constraint	Part weights, dimensions, dispatch lists per trailer
Buying lengths and sizes	Replay shows size choice drives remnants	Purchase sizes against cut lists
Estimation feedback	Baseline loss by product exists	Bid allowances against measured loss
Cross-project plate sharing	Your team rules on cost loading	Remnants valued at book cost, project demand

D Prototype, and what building it changed

A WORKING PAGE AT PROTOTYPE/INDEX.HTML

A working prototype is at prototype/index.html. It is deliberately not a nesting optimiser. It runs the real deterministic packer from analysis/packer.js inside the page, lays the same 15 synthetic parts on one 3000 × 2000 × 12 mm plate under three capabilities, and lets you switch between them.

ARM	RECOVERABLE	NET LOSS	OFFCUT
Hand nest, today	58.2%	0.236 t	not logged
Strumis auto, defaults	58.2%	0.236 t	not logged
Yield Advisor	**88.7%**	**0.064 t**	**registered**

What it does not prove: the geometry is invented, one plate is a bug report and not a baseline, and a real solver would beat every arm shown. 13 assertions cover every figure the page displays.

THE FINDING THAT CHANGED MY RECOMMENDATION

I expected the Advisor's advantage to come from nesting more tightly. **It does not.**

The software arms consume **380 mm less plate height** than the hand nest and recover exactly **0.000 t**, because the material saved comes back as a leftover nobody measures.

All **0.172 t** of recoverable gain comes from writing down where the offcut is.

That is why the week-4 replay should report **packing gain and offcut-recovery gain as two separate numbers**. Expect the first to come back near zero, and do not let a small total be explained away as a solver problem.

IF YOU READ NOTHING ELSE

Read Figure 1 for where your six areas land, Figure 6 for the gate you are agreeing to, and the two cost tables on page 5 for what it costs and what it returns. Everything else supports those three.

E What we are not claiming

STATED PLAINLY, BECAUSE A NUMBER YOU CANNOT DEFEND IS WORSE THAN NO NUMBER

NOT CLAIMED

That the Advisor will hit 1.0 percentage point. The threshold is 0.5 and the conservative case is built on 0.5. Anything above that is upside, not plan.

NOT CLAIMED

That cross-project plate sharing will be permitted. Our value case excludes it entirely, so it cannot be quietly added later to rescue a shortfall.

NOT CLAIMED

That the gain lands in this financial year. Material is bought before the nest exists, so savings appear one purchase cycle after roll-out.

NOT CLAIMED

That we will beat your nesters. If the hand nests win at week 4, we say so, publish the measurement, and stop building.

NOT CLAIMED

That the pilot generalises. Two live projects are a check on buildability, not proof across 10 to 15 concurrent projects.

NOT CLAIMED

That a language model will label revision causes correctly. An engineer confirms every label, so accuracy becomes a measured number, not an assumption.

WHAT I WOULD ASK YOU TO DECIDE IN THE FIRST FORTNIGHT

1. Name the person who approves a nest. Everything else waits on that one answer.

2. Release the read-only Strumis export, so the replay can start in week 3 rather than week 6.

3. Ask your team the cost-loading question, because the largest pool in this case is closed until they answer it.

4. Send the 12-month tonnage export, which costs you one query and tells us which material your case rests on.

WHAT HAPPENS IF YOU SAY NO TO ALL OF IT

You keep the fleet report format, the cause code on remake orders, the 12-month tonnage split, and a written answer to whether your own figures are consistent. Those four things cost almost nothing and are the parts of this engagement most likely to survive a change of mind.

Prepared by your Forward Deployed Engineer, 9 October 2026. Sixteen weeks, fixed price INR 55 lakh, stop gate at week 4.
